Project: 20260929_WPO_BOP1_TMP_Schedule

Seadrill

Print Date: 2026-Oct-15 10:17
Data Date: 2026-Oct-15


Activity ID	Activity Name	% Complete	Original Duration	Remaining Duration	Variance Project Duration	Start	Finish	Job Plan Number	PM Number	WO Number	Crane Access Required
2270-BWM-2026-2 20260929_WPO_BOP1_TMP_Sch		89.25%	460.0h	50.0h	-116.0h	2026-Sep-28 04:00 A	2026-Oct-17 08:00				
2270-BWM-2026-2.3 PRE MAINTENANCE		100%	110.0h	0.0h	0.0h	2026-Sep-28 04:00 A	2026-Oct-02 18:00 A				
A1000	UNLATCH BOP	100%	0.0h	0.0h	0.0h	2026-Sep-28 04:00 A	2026-Sep-28 04:00 A				
A1010	JET BOP	100%	4.0h	0.0h	0.0h	2026-Sep-28 04:00 A	2026-Sep-28 08:00 A				
A1020	PULL RISER	100%	106.0h	0.0h	0.0h	2026-Sep-28 08:00 A	2026-Oct-02 18:00 A				
2270-BWM-2026-2.2 BOP ON BEAMS		96.72%	350.0h	50.0h	-116.0h	2026-Oct-02 18:00 A	2026-Oct-17 08:00				
A1030	BOP ON BEAMS (MAINTENANCE START)	100%	0.0h	0.0h	0.0h	2026-Oct-02 18:00 A	2026-Oct-02 18:00 A				
A1040	TRAVERSE BOP TO SETBACK	100%	8.0h	0.0h	0.0h	2026-Oct-02 18:00 A	2026-Oct-03 02:00 A				
A1350	PRESSURE WASH EXTERIOR WITH FRESH WATER (BEST PRACTIC	100%	1.0h	0.0h	0.0h	2026-Oct-03 02:00 A	2026-Oct-03 03:00 A				
A1360	KETSEATING INSPECTION	100%	3.0h	0.0h	0.0h	2026-Oct-03 03:00 A	2026-Oct-03 06:00 A				
A1370	SPLIT BOP	100%	6.0h	0.0h	0.0h	2026-Oct-03 06:00 A	2026-Oct-03 12:00 A				
A1550	LMRP Work Complete	0%	0.0h	0.0h	0.0h		2026-Oct-13 07:30 A				
A2260	Lower Stack Work Complete	0%	0.0h	0.0h	0.0h		2026-Oct-15 08:24				
A2760	BOP Controls Work Complete	0%	0.0h	0.0h	0.0h		2026-Oct-15 06:00				
A3910	Surface Equipment/Offline Maintenance Completed	0%	0.0h	0.0h	0.0h		2026-Oct-17 08:00				
A3911	Pre Deployment Testing Complete (BOP READY)	0%	0.0h	0.0h	0.0h		2026-Oct-15 21:48				
2270-BWM-2026-2.2.1 BOP MAINTENANCE AND TESTING		96.65%	331.0h	15.8h	-81.8h	2026-Oct-03 02:00 A	2026-Oct-15 21:48				
2270-BWM-2026-2.2.1.1 LOWER STACK		99%	163.0h	2.4h	-171.4h	2026-Oct-03 02:00 A	2026-Oct-15 08:24				
2270-BWM-2026-2.2.1.1.1 UBSR		100%	65.0h	0.0h	-54.0h	2026-Oct-03 02:00 A	2026-Oct-05 19:00 A				
A1561	BWM BLIND SHEAR RAM	100%	3.0h	0.0h	-52.0h	2026-Oct-03 02:00 A	2026-Oct-05 09:00 A	0900-UB0201	C101309		
A1590	BWM BLIND SHEAR RAM DOOR INSPECTION	100%	5.0h	0.0h	-49.0h	2026-Oct-03 05:00 A	2026-Oct-05 11:00 A	0900-UB0205	C275941		
A1595	BWM BLIND SHEAR RAM DOOR INSPECTION	100%	5.0h	0.0h	-49.0h	2026-Oct-03 05:00 A	2026-Oct-05 11:00 A	0900-UB0205	C275988		
A1620	12M SHEAR RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	4.0h	0.0h	0.0h	2026-Oct-05 11:00 A	2026-Oct-05 15:00 A	0900-UB0212	C275943		
A1630	12M SHEAR RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	4.0h	0.0h	0.0h	2026-Oct-05 15:00 A	2026-Oct-05 19:00 A	0900-UB0212	C275990		
2270-BWM-2026-2.2.1.1.2 CSR		100%	59.0h	0.0h	-37.0h	2026-Oct-03 10:00 A	2026-Oct-05 21:00 A				
A1600	BWM CASING SHEAR RAM	100%	3.0h	0.0h	-44.0h	2026-Oct-03 10:00 A	2026-Oct-05 09:00 A	0900-UB0202	C101297		
A1632	BWM BLIND SHEAR RAM DOOR INSPECTION	100%	5.0h	0.0h	-41.0h	2026-Oct-03 13:00 A	2026-Oct-05 11:00 A	0900-UB0205	C275996		
A1633	BWM BLIND SHEAR RAM DOOR INSPECTION	100%	5.0h	0.0h	-41.0h	2026-Oct-03 13:00 A	2026-Oct-05 11:00 A	0900-UB0205	C275992		
A1675	12M CASING SHEAR RAM BLOCKS NDE INSPECTION	100%	7.0h	0.0h	-36.0h	2026-Oct-03 18:00 A	2026-Oct-05 13:00 A	0900-UB90222	C273776		
A1680	12M CASING SHEAR RAM BLOCKS NDE INSPECTION	100%	7.0h	0.0h	-29.0h	2026-Oct-04 01:00 A	2026-Oct-05 13:00 A	0900-UB90222	C273775		
A1690	12M SHEAR RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	4.0h	0.0h	0.0h	2026-Oct-05 13:00 A	2026-Oct-05 17:00 A	0900-UB0212	C275998		
A1695	12M SHEAR RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	4.0h	0.0h	0.0h	2026-Oct-05 17:00 A	2026-Oct-05 21:00 A	0900-UB0212	C275994		
2270-BWM-2026-2.2.1.1.3 LBSR		100%	36.0h	0.0h	-17.0h	2026-Oct-04 08:00 A	2026-Oct-05 20:00 A				
A1700	BWM BLIND SHEAR RAM	100%	3.0h	0.0h	-22.0h	2026-Oct-04 08:00 A	2026-Oct-05 09:00 A	0900-UB0201	C35877		
A1705	BWM BLIND SHEAR RAM DOOR INSPECTION	100%	5.0h	0.0h	-22.0h	2026-Oct-04 08:00 A	2026-Oct-05 11:00 A	0900-UB0205	C276000		
A1710	BWM BLIND SHEAR RAM DOOR INSPECTION	100%	5.0h	0.0h	-22.0h	2026-Oct-04 08:00 A	2026-Oct-05 11:00 A	0900-UB0205	C276004		
A1725	BWM 14" POSLOCK X 14" BOOSTER BLIND SHEAR RAM	100%	3.0h	0.0h	0.0h	2026-Oct-05 09:00 A	2026-Oct-05 12:00 A	0900-UB0239	C259607		
A1740	12M SHEAR RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	4.0h	0.0h	0.0h	2026-Oct-05 12:00 A	2026-Oct-05 16:00 A	0900-UB0212	C276006		
A1745	12M SHEAR RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	4.0h	0.0h	0.0h	2026-Oct-05 16:00 A	2026-Oct-05 20:00 A	0900-UB0212	C276002		
2270-BWM-2026-2.2.1.1.5 UPR		100%	122.0h	0.0h	-102.0h	2026-Oct-04 16:00 A	2026-Oct-09 18:00 A				
A1750	BWM PIPE AND TEST RAMS	100%	4.0h	0.0h	-14.0h	2026-Oct-04 16:00 A	2026-Oct-05 10:00 A	0900-UB0204	C101337		
A1755	BWM PIPE AND TEST RAM DOOR INSPECTION	100%	4.0h	0.0h	-14.0h	2026-Oct-04 16:00 A	2026-Oct-05 10:00 A	0900-UB0208	C192253		
A1760	BWM PIPE AND TEST RAM DOOR INSPECTION	100%	4.0h	0.0h	-14.0h	2026-Oct-04 16:00 A	2026-Oct-05 10:00 A	0900-UB0208	C101339		
A1775	12M PIPE RAM BLOCK INSPECTION	100%	5.0h	0.0h	-10.0h	2026-Oct-04 20:00 A	2026-Oct-05 11:00 A	0900-UB0214	C101347		
A1780	12M PIPE RAM BLOCK INSPECTION	100%	5.0h	0.0h	-10.0h	2026-Oct-04 20:00 A	2026-Oct-05 11:00 A	0900-UB0214	C101349		
A1785	12M PIPE AND TEST RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	3.0h	0.0h	0.0h	2026-Oct-07 18:00 A	2026-Oct-07 21:00 A	0900-UB0216	C192255		
A1790	12M PIPE AND TEST RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	3.0h	0.0h	0.0h	2026-Oct-07 21:00 A	2026-Oct-08 00:00 A	0900-UB0216	C101341		
A1810	(Break in) UPR BOP Door AFT Hinge replacement	100%	12.0h	0.0h	-12.0h	2026-Oct-09 06:00 A	2026-Oct-09 18:00 A				
2270-BWM-2026-2.2.1.1.6 MPR		100%	14.0h	0.0h	-9.0h	2026-Oct-04 01:00 A	2026-Oct-05 14:00 A				
A1795	BWM PIPE AND TEST RAMS	100%	4.0h	0.0h	-29.0h	2026-Oct-04 01:00 A	2026-Oct-05 10:00 A	0900-UB0204	C101351		
A1800	BWM PIPE AND TEST RAM DOOR INSPECTION	100%	4.0h	0.0h	-29.0h	2026-Oct-04 01:00 A	2026-Oct-05 10:00 A	0900-UB0208	C192258		
A1805	BWM PIPE AND TEST RAM DOOR INSPECTION	100%	4.0h	0.0h	-29.0h	2026-Oct-04 01:00 A	2026-Oct-05 10:00 A	0900-UB0208	C192263		
A1820	12M PIPE RAM BLOCK INSPECTION	100%	5.0h	0.0h	-25.0h	2026-Oct-04 05:00 A	2026-Oct-05 11:00 A	0900-UB0214	C101361		
A1825	12M PIPE RAM BLOCK INSPECTION	100%	5.0h	0.0h	-20.0h	2026-Oct-04 10:00 A	2026-Oct-05 11:00 A	0900-UB0214	C101363		
A1830	12M ILF PIPE RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	3.0h	0.0h	0.0h	2026-Oct-05 11:00 A	2026-Oct-05 14:00 A	0900-UB0231	C192266		



Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work

Date	Revision	Checked	Approved
	Full Schedule For Review		

Activity ID	Activity Name	% Complete	Original Duration	Remaining Duration	Variance Project Duration	Start	Finish	Job Plan Number	PM Number	WO Number	Crane Access Required
2270-BWM-2026-2.2.1.1.7 LPR		100%	23.0h	0.0h	18.0h	2026-Oct-04 15:00 A	2026-Oct-05 12:00 A				
A1835	BWM PIPE AND TEST RAMS	100%	4.0h	0.0h	-15.0h	2026-Oct-04 15:00 A	2026-Oct-05 10:00 A	0900-UB0204	C101365		
A1840	BWM PIPE AND TEST RAM DOOR INSPECTION	100%	4.0h	0.0h	-15.0h	2026-Oct-04 15:00 A	2026-Oct-05 10:00 A	0900-UB0208	C276008		
A1845	BWM PIPE AND TEST RAM DOOR INSPECTION	100%	4.0h	0.0h	-15.0h	2026-Oct-04 15:00 A	2026-Oct-05 10:00 A	0900-UB0208	C276012		
A1860	12M PIPE RAM BLOCK INSPECTION	100%	5.0h	0.0h	-11.0h	2026-Oct-04 19:00 A	2026-Oct-05 11:00 A	0900-UB0214	C101375		
A1865	12M PIPE RAM BLOCK INSPECTION	100%	5.0h	0.0h	-6.0h	2026-Oct-05 00:00 A	2026-Oct-05 11:00 A	0900-UB0214	C101377		
A1870	12M PIPE AND TEST RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	3.0h	0.0h	0.0h	2026-Oct-05 06:00 A	2026-Oct-05 09:00 A	0900-UB0216	C276010		
A1875	12M PIPE AND TEST RAM HYDRAULIC OPERATOR CHAMBER TEST	100%	3.0h	0.0h	0.0h	2026-Oct-05 09:00 A	2026-Oct-05 12:00 A	0900-UB0216	C276014		
2270-BWM-2026-2.2.1.1.8 WELLHEAD CONNECTOR		85%	37.0h	1.2h	-254.2h	2026-Oct-04 09:00 A	2026-Oct-15 07:12				
A2130	BWM WELLHEAD CONNECTOR INSPECTION	70%	4.0h	1.2h	-177.2h	2026-Oct-07 18:00 A	2026-Oct-15 07:12	0900-UC0103	C276035		
A2140	12M EVO WELLHEAD CONNECTOR OPERATING CHAMBER TEST /	100%	4.0h	0.0h	0.0h	2026-Oct-04 09:00 A	2026-Oct-04 13:00 A	0900-UC0112	C276033		
2270-BWM-2026-2.2.1.1.9 FAILSAFE VALVES		100%	89.0h	0.0h	-65.0h	2026-Oct-05 10:00 A	2026-Oct-09 19:00 A				
A2150	BWM HYDRAULIC SPRING ASSIST HB GATE VALVES INSPECTION	100%	16.0h	0.0h	-86.0h	2026-Oct-05 10:00 A	2026-Oct-09 16:00 A	0900-RG0201	C101384		
A2160	BWM BOP SUBSEA CHOKE AND KILL SPOOLS INSPECTION	100%	2.0h	0.0h	-33.0h	2026-Oct-08 06:00 A	2026-Oct-09 17:00 A	0900-RH0202	C101453		
A2170	12M HYDRAULIC SPRING ASSIST HB GATE VALVES CHAMBER TES	100%	6.0h	0.0h	-83.0h	2026-Oct-06 02:00 A	2026-Oct-09 19:00 A	0900-RG0203	C101388		
A2180	12M HYDRAULIC SPRING ASSIST HB GATE VALVES CHAMBER TES	100%	6.0h	0.0h	0.0h	2026-Oct-08 09:00 A	2026-Oct-08 15:00 A	0900-RG0203	C101391		
A2190	12M HYDRAULIC SPRING ASSIST HB GATE VALVES CHAMBER TES	100%	6.0h	0.0h	0.0h	2026-Oct-08 15:00 A	2026-Oct-08 21:00 A	0900-RG0203	C101394		
A2200	12M HYDRAULIC SPRING ASSIST HB GATE VALVES CHAMBER TES	100%	6.0h	0.0h	0.0h	2026-Oct-08 21:00 A	2026-Oct-09 03:00 A	0900-RG0203	C275985		
2270-BWM-2026-2.2.1.1.10 LOWER STACK MISC.		93.33%	18.0h	1.2h	-134.4h	2026-Oct-09 00:00 A	2026-Oct-15 08:24				
A2210	BWM BOP BOLTING, FLANGES AND CLAMPS INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-09 03:00 A	2026-Oct-09 05:00 A	0900-UH0101	C101280		
A2230	BWM RISER ADAPTER	100%	2.0h	0.0h	0.0h	2026-Oct-09 03:00 A	2026-Oct-09 05:00 A	0900-UR0202	C276030		
A2240	BWM HYDRAULIC SPRING ASSIST HB GATE MUD BOOST	100%	2.0h	0.0h	0.0h	2026-Oct-09 03:00 A	2026-Oct-09 05:00 A	0900-UR0202	C275979		
A2250	12M RISER ADAPTER - NDE	90%	12.0h	1.2h	-140.4h	2026-Oct-09 00:00 A	2026-Oct-15 08:24	0900-UR0205	C276029		
2270-BWM-2026-2.2.1.4 LMRP		100%	113.0h	0.0h	-123.5h	2026-Oct-04 10:00 A	2026-Oct-13 07:30 A				
2270-BWM-2026-2.2.1.4.2 Upper Annular		100%	60.0h	0.0h	-172.5h	2026-Oct-05 15:00 A	2026-Oct-13 07:30 A				
A1380	BWM ANNULAR BOP INSPECTION	100%	9.0h	0.0h	-31.5h	2026-Oct-07 18:00 A	2026-Oct-09 10:30 A	0900-UA0201	C101458		
A1390	12M ANNULAR BOP CHAMBER TEST	100%	3.0h	0.0h	-181.5h	2026-Oct-05 15:00 A	2026-Oct-13 07:30 A	0900-UA0203	C101460		
2270-BWM-2026-2.2.1.4.1 Lower Annular		100%	58.5h	0.0h	-82.5h	2026-Oct-05 22:00 A	2026-Oct-09 15:30 A				
A1400	BWM ANNULAR BOP INSPECTION	100%	4.0h	0.0h	-29.5h	2026-Oct-08 04:30 A	2026-Oct-09 14:00 A	0900-UA0201	C101293		
A1410	12M ANNULAR BOP CHAMBER TEST	100%	3.0h	0.0h	-86.5h	2026-Oct-05 22:00 A	2026-Oct-09 15:30 A	0900-UA0203	C101295		
2270-BWM-2026-2.2.1.4.3 LMRP Connectors		100%	29.5h	0.0h	-19.5h	2026-Oct-08 14:00 A	2026-Oct-09 19:30 A				
A1430	BWM BOP ADAPTER SPOOL / SUB INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-09 15:30 A	2026-Oct-09 19:30 A	0900-UE0201	C275982		
A1445	12M OPERATOR CHAMBER TEST AND SIGNATURE TEST	100%	6.0h	0.0h	0.0h	2026-Oct-08 14:00 A	2026-Oct-08 20:00 A				
2270-BWM-2026-2.2.1.4.8 LMRP FAILSAFE VALVES &SPOOLS		100%	36.0h	0.0h	-30.5h	2026-Oct-07 02:00 A	2026-Oct-09 20:30 A				
A1446	BWM BOP SUBSEA CHOKE AND KILL SPOOLS INSPECTION	100%	2.0h	0.0h	-22.5h	2026-Oct-08 20:00 A	2026-Oct-09 20:30 A	0900-RH0202	C101453		
A1447	BWM HYDRAULIC SPRING ASSIST HB GATE VALVES INSPECTION	100%	16.0h	0.0h	0.0h	2026-Oct-07 22:00 A	2026-Oct-08 14:00 A	0900-RG0201	C101437		
A1450	12M HYDRAULIC SPRING ASSIST HB GATE VALVES CHAMBER TES	100%	6.0h	0.0h	-24.0h	2026-Oct-07 14:00 A	2026-Oct-08 20:00 A	0900-RG0203	C101438		
A1460	12M HYDRAULIC SPRING ASSIST HB GATE VALVES CHAMBER TES	100%	6.0h	0.0h	0.0h	2026-Oct-07 20:00 A	2026-Oct-08 02:00 A	0900-RG0203	C101441		
A1470	12M HYDRAULIC SPRING ASSIST HB GATE VALVES CHAMBER TES	100%	6.0h	0.0h	-24.0h	2026-Oct-07 02:00 A	2026-Oct-08 08:00 A	0900-RG0203	C101444		
2270-BWM-2026-2.2.1.4.9 CHOKE & KILL STABS		100%	2.0h	0.0h	0.0h	2026-Oct-09 20:30 A	2026-Oct-09 22:30 A				
A1500	12M CHOKE AND KILL LINE NON-LOCKING STAB ASSEMBLY OPER/	100%	2.0h	0.0h	0.0h	2026-Oct-09 20:30 A	2026-Oct-09 22:30 A	0900-UC0207	C276017		
2270-BWM-2026-2.2.1.4.4 LMRP Misc.		100%	51.0h	0.0h	-76.0h	2026-Oct-04 10:00 A	2026-Oct-08 13:00 A				
A1510	(Corrective) NDT Inspection of LMRP Lifting Padeyes	100%	3.0h	0.0h	0.0h	2026-Oct-08 10:00 A	2026-Oct-08 13:00 A			C10248480	
A1520	BWM LMRP VETCO H4 CONNECTOR INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-04 10:00 A	2026-Oct-04 14:00 A	0900-UC0127	C276025		
A1530	BWM BOP BOLTING, FLANGES AND CLAMPS INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-07 18:00 A	2026-Oct-07 22:00 A	0900-UH0101	C101421		
A1540	BOP AND LMRP PADEYES NDE INSPECTION	100%	12.0h	0.0h	0.0h	2026-Oct-07 22:00 A	2026-Oct-08 10:00 A				
2270-BWM-2026-2.2.1.5 BOP Controls		96.97%	255.0h	12.0h	-169.0h	2026-Oct-04 03:00 A	2026-Oct-15 18:00				
2270-BWM-2026-2.2.1.5.1 Blue Pod		100%	255.0h	0.0h	-210.0h	2026-Oct-04 03:00 A	2026-Oct-14 18:00 A				
A2271	BWM MUX CONTROL POD	100%	12.0h	0.0h	-30.0h	2026-Oct-07 18:00 A	2026-Oct-09 12:00 A	0900-UP0205	C275949		
A2275	(Break in) Replace Faulty PT-7 On Blue Pod - Upper annular Pilot Pressur	100%	12.0h	0.0h	-12.0h	2026-Oct-09 12:00 A	2026-Oct-10 00:00 A				
A2280	BWM INTERCONNECTING CABLES AND SENSORS ELECTRICAL IN	100%	6.0h	0.0h	0.0h	2026-Oct-10 00:00 A	2026-Oct-10 06:00 A	0900-QT0201	C101467		
A2290	BWM MUX POD S.E.A ELECTRICAL INSPECTION	100%	3.0h	0.0h	0.0h	2026-Oct-10 00:00 A	2026-Oct-10 03:00 A	0900-UP0210	C101470		
A2300	BWM MUX POD COMPENSATED HOUSING ELECTRICAL INSPECTI(	100%	4.0h	0.0h	0.0h	2026-Oct-10 00:00 A	2026-Oct-10 04:00 A	0900-UP0209	C101475		
A2310	BWM PRE-CHARGE POD PILOT ACCUMULATORS	100%	3.0h	0.0h	0.0h	2026-Oct-10 04:00 A	2026-Oct-10 07:00 A	0900-BT0205	C101478		
A2320	BWM HYDRAULIC SHUTTLE VALVE FUNCTIONALITY TEST	100%	1.0h	0.0h	0.0h	2026-Oct-10 07:00 A	2026-Oct-10 08:00 A	0900-UP0206	C101480		

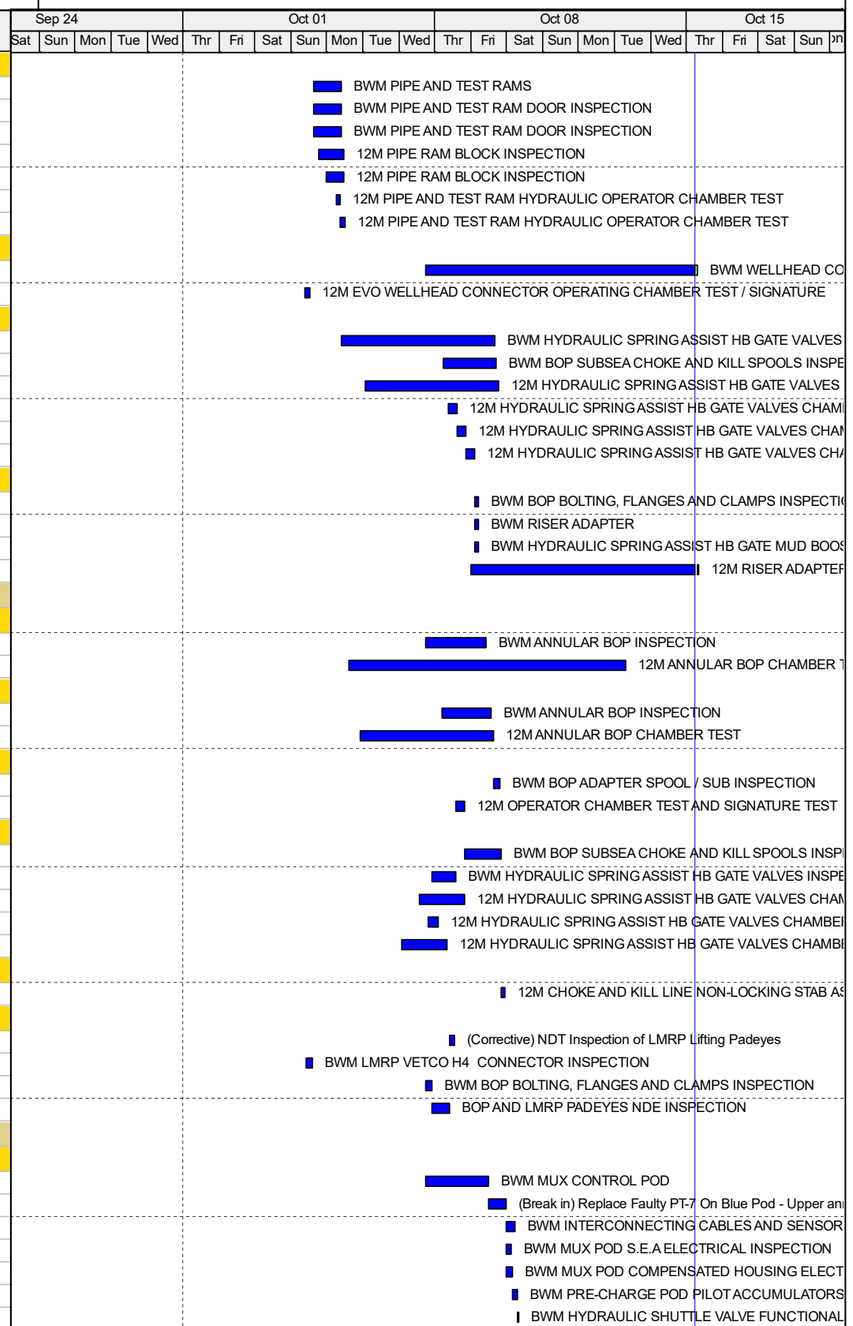

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone


Date	Revision	Checked	Approved
	Full Schedule For Review		

Project: 20260929_WPO_BOP1_TMP_Schedule

Seadrill

Print Date: 2026-Oct-15 10:17
Data Date: 2026-Oct-15

Activity ID	Activity Name	% Complete	Original Duration	Remaining Duration	Variance Project Duration	Start	Finish	Job Plan Number	PM Number	WO Number	Crane Access Required
A2330	BWM CHECK VALVE AND ISOLATION VALVE FUNCTIONALITY/INTEC	100%	2.0h	0.0h	0.0h	2026-Oct-10 07:00 A	2026-Oct-10 09:00 A	0900-UP0207	C101481		
A2340	BWM BOP CONTROL HOSES AND PIPING	100%	6.0h	0.0h	0.0h	2026-Oct-10 09:00 A	2026-Oct-10 15:00 A	0900-UP0105	C101482		
A2350	BWM MUX CABLE AND SUPERBOMB CONNECTOR ELECTRICAL IN	100%	12.0h	0.0h	0.0h	2026-Oct-10 15:00 A	2026-Oct-11 03:00 A	0900-UP0208	C101586		
A2360	(Break in) Superbomb check valve replacement	100%	12.0h	0.0h	-12.0h	2026-Oct-14 06:00 A	2026-Oct-14 18:00 A				
A2370	Troubleshooting pilot pressure alarm above 3300psi	100%	6.0h	0.0h	0.0h	2026-Oct-04 03:00 A	2026-Oct-04 09:00 A				
2270-BWM-2026-2.2.1.5.2	Yellow Pod	100%	120.0h	0.0h	-99.0h	2026-Oct-04 15:00 A	2026-Oct-10 15:00 A				
A2380	BWM MUX CONTROL POD	100%	12.0h	0.0h	-30.0h	2026-Oct-07 18:00 A	2026-Oct-09 12:00 A	0900-UP0205	C275952		
A2390	BWM INTERCONNECTING CABLES AND SENSORS ELECTRICAL IN	100%	6.0h	0.0h	0.0h	2026-Oct-09 12:00 A	2026-Oct-09 18:00 A	0900-QT0201	C101492		
A2400	BWM MUX POD S.E.A ELECTRICAL INSPECTION	100%	3.0h	0.0h	0.0h	2026-Oct-09 12:00 A	2026-Oct-09 15:00 A	0900-UP0210	C101495		
A2410	BWM MUX POD COMPENSATED HOUSING ELECTRICAL INSPECTI	100%	4.0h	0.0h	0.0h	2026-Oct-09 12:00 A	2026-Oct-09 16:00 A	0900-UP0209	C101500		
A2420	BWM PRE-CHARGE POD PILOT ACCUMULATORS	100%	3.0h	0.0h	0.0h	2026-Oct-09 16:00 A	2026-Oct-09 19:00 A	0900-BT0205	C101503		
A2430	BWM HYDRAULIC SHUTTLE VALVE FUNCTIONALITY TEST	100%	1.0h	0.0h	0.0h	2026-Oct-09 19:00 A	2026-Oct-09 20:00 A	0900-UP0206	C101505		
A2440	BWM CHECK VALVE AND ISOLATION VALVE FUNCTIONALITY/INTEC	100%	2.0h	0.0h	0.0h	2026-Oct-09 19:00 A	2026-Oct-09 21:00 A	0900-UP0207	C101506		
A2450	BWM BOP CONTROL HOSES AND PIPING	100%	6.0h	0.0h	0.0h	2026-Oct-09 21:00 A	2026-Oct-10 03:00 A	0900-UP0105	C101507		
A2460	BWM MUX CABLE AND SUPERBOMB CONNECTOR ELECTRICAL IN	100%	12.0h	0.0h	0.0h	2026-Oct-10 03:00 A	2026-Oct-10 15:00 A	0900-UP0208	C101593		
A2470	Troubleshooting pilot pressure alarm above 3300psi	100%	6.0h	0.0h	0.0h	2026-Oct-04 15:00 A	2026-Oct-04 21:00 A				
2270-BWM-2026-2.2.1.5.3	Acoustic Control Pod	100%	105.0h	0.0h	-75.0h	2026-Oct-08 09:00 A	2026-Oct-11 18:00 A				
A2480	BWM ACOUSTIC CONTROL POD	100%	2.0h	0.0h	0.0h	2026-Oct-08 09:00 A	2026-Oct-08 11:00 A	0900-UP0202	C276515		
A2490	BWM ACOUSTIC CONTROL SYSTEM ELECTRICAL INSPECTION	100%	6.0h	0.0h	0.0h	2026-Oct-11 03:00 A	2026-Oct-11 09:00 A	0900-UP0164	C276507		
A2495	(Break in) Acoustic batteries replacement	100%	12.0h	0.0h	-12.0h	2026-Oct-11 06:00 A	2026-Oct-11 18:00 A				
A2500	BWM ACOUSTIC HYD SUPPLY RETRACTABLE STABS	100%	1.0h	0.0h	0.0h	2026-Oct-11 03:00 A	2026-Oct-11 04:00 A	0900-UP0203	C276520		
A2510	12M OPERATOR CHAMBER TEST	100%	3.0h	0.0h	0.0h	2026-Oct-11 04:00 A	2026-Oct-11 07:00 A				
2270-BWM-2026-2.2.1.5.6	EHBS Pod	100%	4.0h	0.0h	0.0h	2026-Oct-11 07:00 A	2026-Oct-11 11:00 A				
A2520	BWM EHBS CONTROL POD INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-11 07:00 A	2026-Oct-11 11:00 A	0900-UP0211	C101530		
2270-BWM-2026-2.2.1.5.7	Accumulators	100%	27.0h	0.0h	0.0h	2026-Oct-11 11:00 A	2026-Oct-12 14:00 A				
A2530	BWM STACK MOUNTED ACCUMULATORS INSPECTION BOP 1	100%	2.0h	0.0h	0.0h	2026-Oct-11 11:00 A	2026-Oct-11 13:00 A	0900-BT0211	C36275		
A2540	BWM STACK MOUNTED ACCUMULATORS (DCB) INSPECTION BOP	100%	12.0h	0.0h	0.0h	2026-Oct-11 13:00 A	2026-Oct-12 01:00 A	0900-BT0210	C277015		
A2550	BWM LMRP MOUNTED BLADDER ACCUMULATORS (15 Gallons) INS	100%	6.0h	0.0h	0.0h	2026-Oct-12 01:00 A	2026-Oct-12 07:00 A	0900-BT80021	C231878		
A2560	BWM STACK MOUNTED BLADDER ACCUMULATOR (15 Gallon) INSP	100%	6.0h	0.0h	0.0h	2026-Oct-12 07:00 A	2026-Oct-12 13:00 A	0900-BT80021	C231880		
A2570	3M SURFACE ACCUMULATORS INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-12 13:00 A	2026-Oct-12 14:00 A	0900-VW0203	C101645		
2270-BWM-2026-2.2.1.5.8	Failsafe Kits	100%	2.0h	0.0h	0.0h	2026-Oct-12 14:00 A	2026-Oct-12 16:00 A				
A2640	BWM FAILSAFE ASSIST KIT INSPECTION BOP 1	100%	2.0h	0.0h	0.0h	2026-Oct-12 14:00 A	2026-Oct-12 16:00 A	0900-RG0207	C36287		
2270-BWM-2026-2.2.1.5.4	BOP Control Misc.	75.51%	192.0h	12.0h	-232.0h	2026-Oct-04 07:00 A	2026-Oct-15 18:00				
A2650	(Corrective) BOP Pilot Pressure Regulator (Removal and Analysis)	100%	6.0h	0.0h	0.0h	2026-Oct-04 07:00 A	2026-Oct-04 13:00 A				
A2660	BWM BOP UPS ELECTRICAL INSPECTION	100%	3.0h	0.0h	0.0h	2026-Oct-09 06:00 A	2026-Oct-09 09:00 A	0900-EB0101	C280053		
A2670	BWM BOP UPS ELECTRICAL INSPECTION	100%	3.0h	0.0h	0.0h	2026-Oct-09 09:00 A	2026-Oct-09 12:00 A	0900-EB0101	C280036		
A2680	BWM CATHODIC PROTECTION ELECTRICAL INSPECTION	100%	5.0h	0.0h	0.0h	2026-Oct-09 12:00 A	2026-Oct-09 17:00 A	0900-UP0260	C101463		
A2690	BWM WELLBORE PT WET MATE CONNECTOR INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-09 17:00 A	2026-Oct-09 18:00 A	0900-UP0218	C101526		
A2700	12M WELLBORE PT WET MATE CONNECTOR HYD CHAMBER TEST	100%	1.0h	0.0h	0.0h	2026-Oct-13 06:00 A	2026-Oct-13 07:00 A	0900-UP0237	C101527		
A2710	12M DIGITAL GAUGES AND PRESSURE TRANSMITTERS	50%	24.0h	12.0h	-35.0h	2026-Oct-13 07:00 A	2026-Oct-15 18:00	0900-QQ0202	C101662		
A2720	BWM RIGID CONDUIT VALVE MANIFOLD (LMRP) INSPECTION	100%	3.0h	0.0h	0.0h	2026-Oct-09 19:00 A	2026-Oct-09 22:00 A	0900-UP0212	C101520		
A2730	BWM HOTLINE VALVE MANIFOLD (LMRP)	100%	1.0h	0.0h	0.0h	2026-Oct-09 22:00 A	2026-Oct-09 23:00 A	0900-UP0213	C101523		
A2740	BWM CONDUIT MANIFOLD (SURFACE) INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-09 23:00 A	2026-Oct-10 00:00 A	0900-UP0214	C101640		
A2750	BWM HOTLINE MANIFOLD (SURFACE) INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-04 07:00 A	2026-Oct-04 08:00 A	0900-UP0215	C101643		
2270-BWM-2026-2.2.1.6	Pre-Deployment Testing	86.99%	103.0h	13.4h	23.2h	2026-Oct-12 14:00 A	2026-Oct-15 21:48				
2270-BWM-2026-2.2.1.6.5	TESTING	86.99%	103.0h	13.4h	23.2h	2026-Oct-12 14:00 A	2026-Oct-15 21:48				
A2770	BWM EHBS FUNCTION TEST - SURFACE	100%	3.0h	0.0h	0.0h	2026-Oct-12 14:00 A	2026-Oct-12 17:00 A	0900-UB0222	C101529		
A2780	BWM BOP SURFACE FUNCTION PRESSURE TEST	100%	48.0h	0.0h	3.8h	2026-Oct-12 17:00 A	2026-Oct-14 13:12 A	0900-UB0108	C101417		
A2790	BWM EDS SURFACE FUNCTION TEST	80%	4.0h	0.8h	-60.2h	2026-Oct-12 17:00 A	2026-Oct-15 09:12	0900-UB0111	C101418		
A2800	BWM BOP CONTROL SYSTEM SURFACE LEAK OFF SOAK TEST	30%	18.0h	12.6h	-13.8h	2026-Oct-14 14:00 A	2026-Oct-15 21:48	0900-UP0201	C101462		
A2810	BWM ACOUSTIC CONTROL SYST. FUNCTION TEST - SURFACE	100%	4.0h	0.0h	0.0h	2026-Oct-12 15:00 A	2026-Oct-12 19:00 A	0900-UB0109	C276518		
A2820	BWM ROV INTERVENTION FUNCTION TEST - SURFACE	100%	12.0h	0.0h	-26.2h	2026-Oct-12 19:00 A	2026-Oct-14 09:12 A	0900-UB0113	C101577		
A2830	BWM INITIAL SUBSEA EMERGENCY ACCUMULATOR DRAWDOWN	100%	6.0h	0.0h	0.0h	2026-Oct-14 09:12 A	2026-Oct-14 15:12 A	0900-BT0201	C101601		
A2840	BWM DRAWDOWN TEST - SURFACE AND SUBSEA	100%	4.0h	0.0h	0.0h	2026-Oct-14 15:12 A	2026-Oct-14 19:12 A	0900-BT0102	C101604		
A2890	BWM BOP SURFACE FUNCTION TEST	100%	4.0h	0.0h	-48.2h	2026-Oct-12 17:00 A	2026-Oct-14 21:12 A	0900-UB0110	C101419		

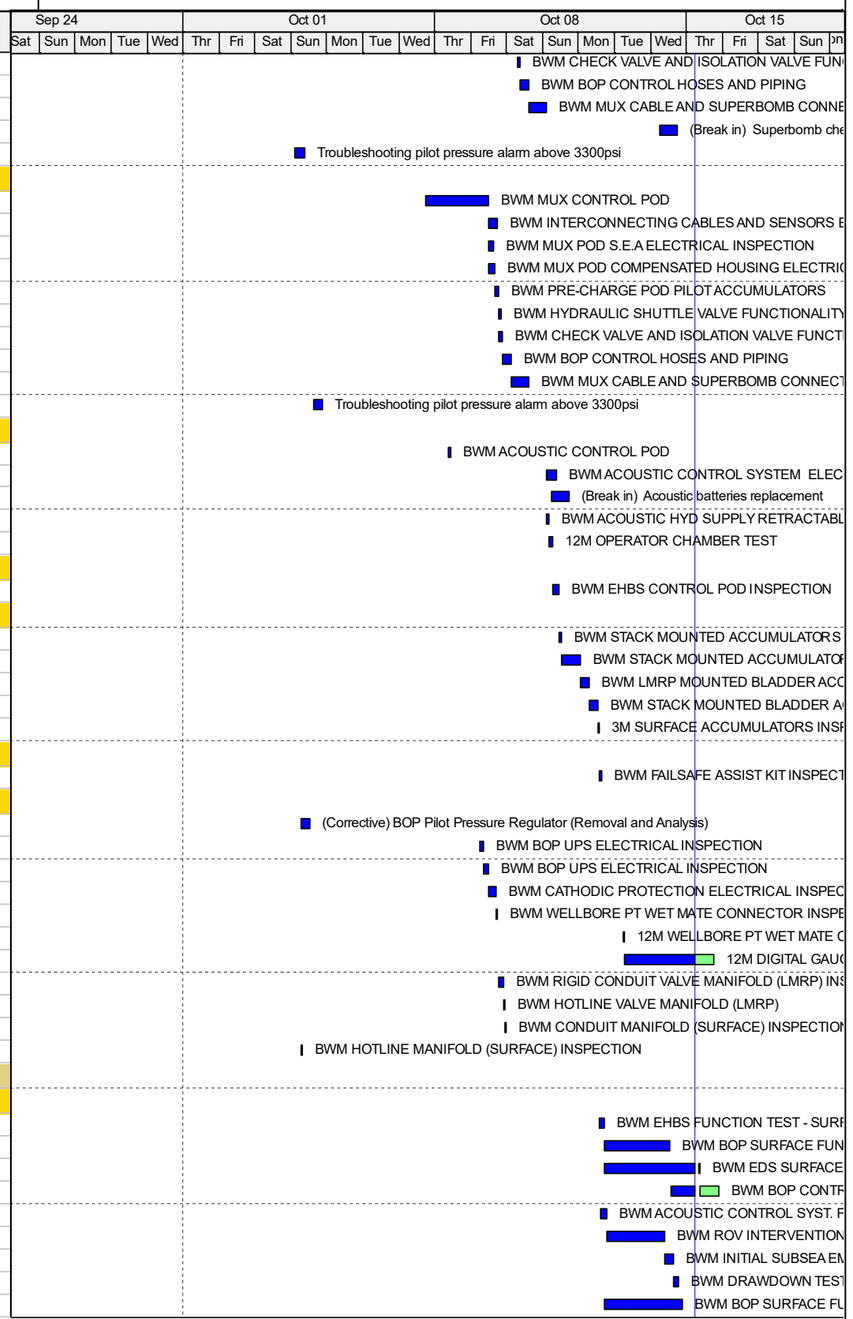

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved
	Full Schedule For Review		

Project: 20260929_WPO_BOP1_TMP_Schedule

Seadrill

Print Date: 2026-Oct-15 10:17
Data Date: 2026-Oct-15

Activity ID	Activity Name	% Complete	Original Duration	Remaining Duration	Variance Project Duration	Start	Finish	Job Plan Number	PM Number	WO Number	Crane Access Required
2270-BWM-2026-2.10 Surface Equipment/Offline Maintenance		81.85%	331.0h	50.0h	-161.0h	2026-Oct-02 18:00 A	2026-Oct-17 08:00				
A2910	Olmsted valve Replacement (AUX CMC)	95%	36.0h	36.0h	-300.0h	2026-Oct-02 18:00 A	2026-Oct-16 18:00				
A3920	WO R10509931 - MRTs - FLUID FILTRATION AND CALIBRATION	50%	100.0h	50.0h	-26.0h	2026-Oct-09 06:00 A	2026-Oct-17 08:00				
2270-BWM-2026-2.10.1 Diverter, Flex Joint, & Riser Adapter		47.62%	126.0h	22.0h	-84.0h	2026-Oct-10 22:00 A	2026-Oct-16 04:00				
A2930	BWM DIVERTER ASSEMBLY (21 1/4" Shaffer) INSPECTION	0%	2.0h	2.0h	0.0h	2026-Oct-15 06:00	2026-Oct-15 08:00	0900-BE0202	C101670		
A2940	BWM DIVERTER SYSTEM FUNCTION TEST-INSTALLATION	0%	2.0h	2.0h	0.0h	2026-Oct-15 08:00	2026-Oct-15 10:00	0900-BE0204	C242980		
A2950	BWM DIVERTER HOUSING INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-10 22:00 A	2026-Oct-11 00:00 A	0900-BE0203	C101667		
A2960	BWM DIVERTER PIPER VALVES INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-11 00:00 A	2026-Oct-11 02:00 A	0900-RB80021	C242979		
A2970	BWM FLEX JOINT (Oil States) INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-11 02:00 A	2026-Oct-11 04:00 A	0900-UK0101	C101687		
A2980	BWM FLEX JOINT (Oil States) INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-11 04:00 A	2026-Oct-11 06:00 A	0900-UK0101	C276027		
A2990	3M DIVERTER PIPER VALVES INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-11 06:00 A	2026-Oct-11 08:00 A	0900-RB0101	C101665		
A3000	12M DIVERTER ASSEMBLY (21 1/4" Shaffer) SERVICE	0%	18.0h	18.0h	0.0h	2026-Oct-15 10:00	2026-Oct-16 04:00	0900-BE0206	C101671		
A3010	6M DIVERTER ACCUMULATORS INSPECTION	100%	6.0h	0.0h	-59.0h	2026-Oct-12 02:00 A	2026-Oct-14 19:00 A	0900-VW0201	C101676		
A3020	12M FLEX JOINT (Oil States) SERVICE	100%	4.0h	0.0h	0.0h	2026-Oct-12 08:00 A	2026-Oct-12 12:00 A	0900-UK0102	C101688		
2270-BWM-2026-2.10.2 Tensioners,Tension Ring, ROPS, Goosen		98.18%	204.0h	6.0h	-70.0h	2026-Oct-05 06:00 A	2026-Oct-15 12:00				
A3030	BWM GOOSENECK ASSEMBLIES INSPECTION	100%	6.0h	0.0h	0.0h	2026-Oct-09 06:00 A	2026-Oct-09 12:00 A	0900-US0205	C36592		
A3040	BWM NOV SHAFFER HF GOOSENECK ASSEMBLY INSPECTION	100%	6.0h	0.0h	0.0h	2026-Oct-08 00:00 A	2026-Oct-08 06:00 A	0900-BR0204	C280738		
A3050	(Corrective) HFGN / Tensioner Ring Maintenance	100%	168.0h	0.0h	38.4h	2026-Oct-05 06:00 A	2026-Oct-10 15:36 A			R10508242	
A3060	BWM NOV TENSION RING ASSEMBLY INSPECTION	100%	6.0h	0.0h	0.0h	2026-Oct-08 06:00 A	2026-Oct-08 12:00 A	0900-BR0201	C101684		
A3070	12M NOV SHAFFER HF GOOSENECK ASSEMBLY INSPECTION	100%	6.0h	0.0h	0.0h	2026-Oct-09 12:00 A	2026-Oct-09 18:00 A	0900-BR0205	C280737		
A3080	Install upgrade funnel with new bolts and nordlock washers - HFGN instal	100%	120.0h	0.0h	-24.0h	2026-Oct-06 06:00 A	2026-Oct-12 06:00 A				
A3090	BWM DUAL WIRELINE RISER TENSIONER SERVICE	100%	6.0h	0.0h	0.0h	2026-Oct-12 06:00 A	2026-Oct-12 12:00 A	0900-MS0803	C35322		
A3100	Troubleshooting RARS valve signal	50%	4.0h	2.0h	-46.0h	2026-Oct-13 06:00 A	2026-Oct-15 08:00				
A3110	Troubleshooting RARS valve signal	50%	4.0h	2.0h	-44.0h	2026-Oct-13 10:00 A	2026-Oct-15 10:00				
A3120	Troubleshooting RARS valve signal	50%	4.0h	2.0h	-42.0h	2026-Oct-13 14:00 A	2026-Oct-15 12:00				
2270-BWM-2026-2.10.3 MoonPool Hoses & Swivels		100%	36.0h	0.0h	0.0h	2026-Oct-07 18:00 A	2026-Oct-09 06:00 A				
A3130	BWM MOONPOOL HP ARMORED HOSE INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-07 18:00 A	2026-Oct-07 19:00 A	0900-RI0108	C279695		
A3140	BWM MOONPOOL HP ARMORED HOSE INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-07 19:00 A	2026-Oct-07 20:00 A	0900-RI0108	C52710		
A3150	BWM HYDRAULIC CONDUIT MOONPOOL HOSE INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-07 20:00 A	2026-Oct-07 21:00 A	0900-RI0112	C52534		
A3160	BWM BLACK EAGLE HYD. CONDUIT JUMPER HOSE BOP 1	100%	1.0h	0.0h	0.0h	2026-Oct-07 21:00 A	2026-Oct-07 22:00 A	0900-RI0102	C36248		
A3170	12M HYDRAULIC CONDUIT MOONPOOL HOSE - NDE INSPECTION	100%	6.0h	0.0h	0.0h	2026-Oct-07 22:00 A	2026-Oct-08 04:00 A	0900-RI0113	C101650		
A3180	12M HYDRAULIC CONDUIT MOONPOOL HOSE - NDE INSPECTION	100%	6.0h	0.0h	0.0h	2026-Oct-08 04:00 A	2026-Oct-08 10:00 A	0900-RI0113	C101653		
A3190	12M MOONPOOL SWIVELS INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-08 10:00 A	2026-Oct-08 14:00 A	0900-US0107	C227879		
A3200	12M MOONPOOL SWIVELS INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-08 14:00 A	2026-Oct-08 18:00 A	0900-US0107	C227880		
A3210	12M MOONPOOL SWIVELS INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-08 18:00 A	2026-Oct-08 22:00 A	0900-US0107	C227882		
A3220	12M MOONPOOL SWIVELS INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-08 22:00 A	2026-Oct-09 02:00 A	0900-US0107	C227884		
A3230	12M MOONPOOL SWIVELS INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-09 02:00 A	2026-Oct-09 06:00 A	0900-US0107	C227885		
2270-BWM-2026-2.10.4 REELS, CONTROL PANELS, SURFACE M/		100%	128.0h	0.0h	-86.0h	2026-Oct-05 06:00 A	2026-Oct-10 14:00 A				
A3240	BWM ROV PANELS - SURFACE	100%	1.0h	0.0h	0.0h	2026-Oct-05 06:00 A	2026-Oct-05 07:00 A	0900-UP0217	C101579		
A3250	BWM HOTLINE MANIFOLD (SURFACE) INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-05 07:00 A	2026-Oct-05 08:00 A	0900-UP0215	C101643		
A3260	BWM REMOTE CONTROL STAND FOR CABLE REELS SUBSEA INSF	100%	2.0h	0.0h	0.0h	2026-Oct-09 06:00 A	2026-Oct-09 08:00 A	0900-UP0220	C101599		
A3270	BWM HOSE REEL AND SHEAVES INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-05 10:00 A	2026-Oct-05 12:00 A	0900-UP0261	C148547		
A3280	BWM MUX REEL ELECTRICAL INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-09 08:00 A	2026-Oct-09 10:00 A	0900-UP0238	C101591		
A3290	BWM MUX REEL ELECTRICAL INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-09 10:00 A	2026-Oct-09 12:00 A	0900-UP0238	C101584		
A3300	BWM BOP CONTROL PANELS ELECTRICAL INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-09 12:00 A	2026-Oct-09 14:00 A	0900-IF0201	C101657		
A3310	BWM CABLE REEL AND SHEAVES INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-05 18:00 A	2026-Oct-05 20:00 A	0900-UP0219	C36431		
A3320	12M CABLE REEL AND SHEAVES SERVICE	100%	2.0h	0.0h	0.0h	2026-Oct-05 20:00 A	2026-Oct-05 22:00 A	0900-UP0221	C101583		
A3330	BWM MUX CABLE AND SUPERBOMB CONNECTOR ELECTRICAL IN	100%	12.0h	0.0h	0.0h	2026-Oct-09 14:00 A	2026-Oct-10 02:00 A	0900-UP0208	C101586		
A3340	12M CABLE REEL AND SHEAVES SERVICE	100%	2.0h	0.0h	0.0h	2026-Oct-06 10:00 A	2026-Oct-06 12:00 A	0900-UP0221	C101590		
A3350	BWM MUX CABLE AND SUPERBOMB CONNECTOR ELECTRICAL IN	100%	12.0h	0.0h	0.0h	2026-Oct-10 02:00 A	2026-Oct-10 14:00 A	0900-UP0208	C101593		
2270-BWM-2026-2.10.5 RISER & DIVERTER HANDLING TOOLS,		100%	14.0h	0.0h	0.0h	2026-Oct-09 06:00 A	2026-Oct-09 20:00 A				
A3360	BWM BOP RETRACTABLE TEST STUMP INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-09 06:00 A	2026-Oct-09 08:00 A	0900-CX0802	C101410		
A3370	BWM NOV SHAFFER HYD. SPIDER GIMBAL AND CONTROL PANEL I	100%	3.0h	0.0h	0.0h	2026-Oct-09 08:00 A	2026-Oct-09 11:00 A	0900-WW0201	C101712		
A3380	BWM DIVERTER HANDLING TOOL INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-09 11:00 A	2026-Oct-09 15:00 A	0900-DP0201	C101678		
A3390	BWM CLOVER RISER TORQUE TOOL INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-09 15:00 A	2026-Oct-09 16:00 A	0900-WW0101	C36588		

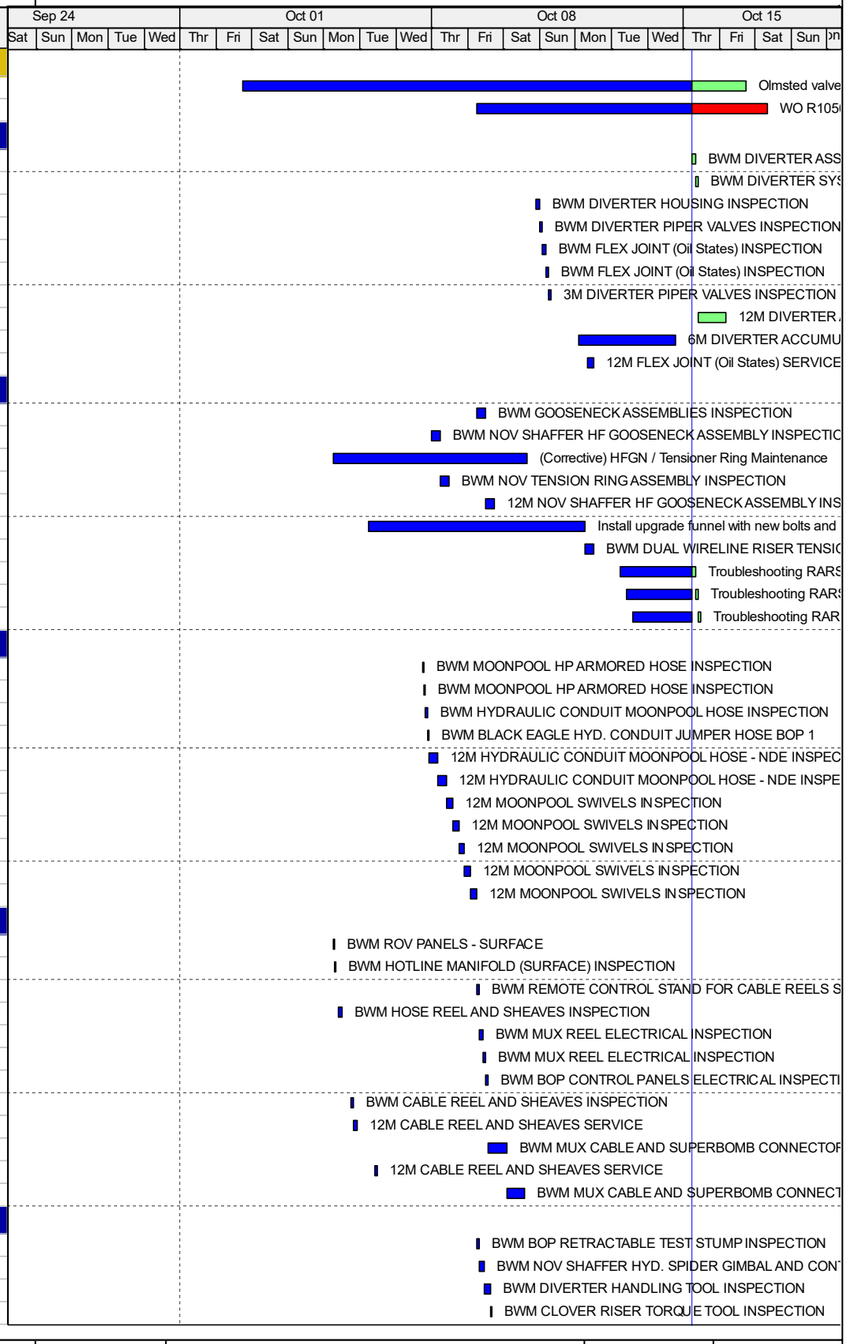

Remaining Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work


Date	Revision	Checked	Approved
	Full Schedule For Review		

Project: 20260929_WPO_BOP1_TMP_Schedule

Seadrill

Print Date: 2026-Oct-15 10:17
Data Date: 2026-Oct-15

Activity ID	Activity Name	% Complete	Original Duration	Remaining Duration	Variance Project Duration	Start	Finish	Job Plan Number	PM Number	WO Number	Crane Access Required
A3400	BWM NOV SHAFFER HYDRAULIC RISER RUNNING TOOL INSPECT	100%	3.0h	0.0h	0.0h	2026-Oct-09 16:00 A	2026-Oct-09 19:00 A	0900-DP0204	C36582		
A3410	BWM BOP HANDLING AND TEST TOOL INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-09 19:00 A	2026-Oct-09 20:00 A	0900-DP0207	C101715		
2270-BWM-2026-2.10.6 RISER & SLIP JOINT		99.12%	97.5h	0.5h	-152.5h	2026-Oct-06 13:00 A	2026-Oct-15 06:30				
A3450	BWM ROMAR TELESCOPIC JOINT PACKER MANAGEMENT SYSTEM	100%	2.0h	0.0h	-95.0h	2026-Oct-09 06:00 A	2026-Oct-13 07:00 A	0900-US0103	C101686		
A3460	BWM NOV SHAFFER FT-H TELESCOPIC JOINT (SHIPS) INSPECTION	100%	8.0h	0.0h	0.0h	2026-Oct-09 08:00 A	2026-Oct-09 16:00 A	0900-US0201	C101693		
A3470	BWM NOV SHAFFER FT-H TELESCOPIC JOINT (SHIPS) INSPECTION	100%	8.0h	0.0h	-81.4h	2026-Oct-09 16:00 A	2026-Oct-13 09:24 A	0900-US0201	C101699		
A3480	BWM NOV SHAFFER FT-H RISER COMMON INSPECTION	100%	36.0h	0.0h	0.0h	2026-Oct-10 00:00 A	2026-Oct-11 12:00 A	0900-UR0201	C101682		
A3490	BWM NOV SHAFFER FT-H RISER CBM INSPECTION	90%	1.0h	0.1h	-89.1h	2026-Oct-11 12:00 A	2026-Oct-15 06:06	0900-UR0209	C273658		
A3500	12M NOV SHAFFER FT-H BASIC RISER CBM - NDE - INSPECTION	90%	1.0h	0.1h	-208.2h	2026-Oct-06 13:00 A	2026-Oct-15 06:12	0900-UR0210	C273659		
A3510	12M NOV SHAFFER FT-H DETAILED/ENHANCED RISER CBM - NDE	70%	1.0h	0.3h	-88.0h	2026-Oct-11 13:30 A	2026-Oct-15 06:30	0900-UR0211	C273660		
2270-BWM-2026-2.10.9 Test Pumps, HPU, & Triplex Pumps		100%	96.0h	0.0h	-87.0h	2026-Oct-05 11:00 A	2026-Oct-09 11:00 A				
A3520	3M BOP HPU PIPEWORK AND VALVES INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-09 06:00 A	2026-Oct-09 07:00 A	0900-RH0201	C101605		
A3530	3M FLUID MIXING SYSTEM INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-09 07:00 A	2026-Oct-09 08:00 A	0900-CJ0201	C101620		
A3540	3M BOP TEST PUMP INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-09 08:00 A	2026-Oct-09 10:00 A	0900-PB0201	C101768		
A3550	12M BOP FLUID RECIRCULATION PUMP INSPECTION	100%	1.0h	0.0h	0.0h	2026-Oct-09 10:00 A	2026-Oct-09 11:00 A	0900-PA0201	C101632		
A3560	Repair surface flow meter	100%	4.0h	0.0h	0.0h	2026-Oct-05 11:00 A	2026-Oct-05 15:00 A				
2270-BWM-2026-2.10.10 Choke & Kill Manifold/Mud Gas Seperat		0%	8.0h	8.0h	0.0h	2026-Oct-15 06:00	2026-Oct-15 14:00				
A3570	3M MUD GAS SEPARATOR INSPECTION	0%	3.0h	3.0h	0.0h	2026-Oct-15 06:00	2026-Oct-15 09:00	0900-BJ0001	C101762		
A3580	12M DIGITAL PRESSURE GAUGES	0%	2.0h	2.0h	0.0h	2026-Oct-15 09:00	2026-Oct-15 11:00	0900-QQ0402	C101739		
A3590	12M MUD GAS SEPARATOR INSPECTION	0%	3.0h	3.0h	0.0h	2026-Oct-15 11:00	2026-Oct-15 14:00	0900-BJ0002	C101763		
2270-BWM-2026-2.10.7 MPD		75.39%	191.0h	31.0h	-26.0h	2026-Oct-07 14:00 A	2026-Oct-16 13:00				
A3600	BWM HIGH PRESSURE HOSE MPD FLM	25%	1.0h	0.8h	-47.8h	2026-Oct-13 06:00 A	2026-Oct-15 06:45	0900-RI8005	C278543		
A3610	BWM MPD HYDRAULIC POWER UNIT INSPECTION AND SERVICE	0%	4.0h	4.0h	0.0h	2026-Oct-15 06:45	2026-Oct-15 10:45	0900-CV90075	C278704		
A3620	BWM HIGH PRESSURE HOSE MPD FLM	25%	1.0h	0.8h	-47.5h	2026-Oct-13 11:00 A	2026-Oct-15 11:30	0900-RI8005	C278546		
A3630	BWM PS37 F01 MPD SYSTEM FUNCTION TEST (ROUTE)	100%	2.0h	0.0h	0.0h	2026-Oct-09 12:00 A	2026-Oct-09 14:00 A	0900-CX99016	C188718		
A3640	BWM IRJ MOUNTED ACCUMULATOR PRE-CHARGE	100%	6.0h	0.0h	0.0h	2026-Oct-09 14:00 A	2026-Oct-09 20:00 A	0900-UR90022	C278534		
A3650	BWM HIGH PRESSURE HOSE MPD FLM	25%	1.0h	0.8h	-47.3h	2026-Oct-13 12:00 A	2026-Oct-15 12:15	0900-RI8005	C275892		
A3660	BWM HIGH PRESSURE HOSE MPD FLM	25%	1.0h	0.8h	-47.0h	2026-Oct-13 13:00 A	2026-Oct-15 13:00	0900-RI8005	C275895		
A3670	BWM IRJ MOUNTED CONTROLS INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-09 22:00 A	2026-Oct-10 02:00 A	0900-IA90064	C277878		
A3680	BWM MPD RCD BEARING ASSEMBLY INSPECTION	100%	12.0h	0.0h	0.0h	2026-Oct-07 14:00 A	2026-Oct-08 02:00 A	0900-BZ90024	C278203		
A3690	BWM MPD RCD BEARING ASSEMBLY INSPECTION	100%	12.0h	0.0h	0.0h	2026-Oct-08 02:00 A	2026-Oct-08 14:00 A	0900-BZ90024	C278205		
A3700	BWM MPD RCD BEARING ASSEMBLY INSPECTION	100%	12.0h	0.0h	0.0h	2026-Oct-08 14:00 A	2026-Oct-09 02:00 A	0900-BZ90024	C278207		
A3710	BWM THIRD PARTY MPD EQUIPMENT INSPECTION	100%	3.0h	0.0h	0.0h	2026-Oct-09 02:00 A	2026-Oct-09 05:00 A	0900-XX90024	C277360		
A3720	BWM THIRD PARTY MPD EQUIPMENT INSPECTION	100%	3.0h	0.0h	0.0h	2026-Oct-09 02:00 A	2026-Oct-09 05:00 A	0900-XX90024	C277361		
A3730	3M MPD HPU ACCUMULATORS FLM	100%	1.0h	0.0h	0.0h	2026-Oct-13 14:00 A	2026-Oct-13 15:00 A	0900-VW8405	C278692		
A3740	3M HYDRAULIC POWER UNIT MPD INSPECTION	100%	2.0h	0.0h	0.0h	2026-Oct-13 15:00 A	2026-Oct-13 17:00 A	0900-CV8022	C278694		
A3750	3M MPD PRV PANEL INSPECTION	100%	4.0h	0.0h	0.0h	2026-Oct-08 11:00 A	2026-Oct-08 15:00 A	0900-IF90022	C277880		
A3760	Accumulator pre-charge (PRV and HCU)	0%	24.0h	24.0h	0.0h	2026-Oct-15 13:00	2026-Oct-16 13:00				
A3770	6M MPD HPU ACCUMULATORS INSPECTION	100%	8.0h	0.0h	0.0h	2026-Oct-13 17:00 A	2026-Oct-14 01:00 A	0900-VW8406	C278693		
A3780	6M LOCAL CONTROL PANEL INSPECTION	0%	2.0h	2.0h	0.0h	2026-Oct-15 13:00	2026-Oct-15 15:00	0900-IF0003	C275899		
A3790	6M INSTRUMENT (PLC / PC) CABINET INSPECTION	0%	1.0h	1.0h	0.0h	2026-Oct-15 15:00	2026-Oct-15 16:00	0900-IA90061	C275897		
A3800	6M LOCAL CONTROL PANEL INSPECTION	0%	2.0h	2.0h	0.0h	2026-Oct-15 16:00	2026-Oct-15 18:00	0900-IF0003	C275900		
A3810	6M LOCAL CONTROL PANEL INSPECTION	0%	2.0h	2.0h	0.0h	2026-Oct-15 18:00	2026-Oct-15 20:00	0900-IF0003	C275898		
A3820	12M MPD RCD BEARING ASSEMBLY INSPECTION	100%	12.0h	0.0h	0.0h	2026-Oct-08 06:00 A	2026-Oct-08 18:00 A	0900-BZ90025	C278202		
A3830	12M MPD RCD BEARING ASSEMBLY INSPECTION	100%	12.0h	0.0h	0.0h	2026-Oct-08 06:00 A	2026-Oct-08 18:00 A	0900-BZ90025	C278204		
A3840	12M MPD RCD BEARING ASSEMBLY INSPECTION	100%	12.0h	0.0h	0.0h	2026-Oct-08 06:00 A	2026-Oct-08 18:00 A	0900-BZ90025	C278206		
A3850	12M LOCAL CONTROL PANEL INSPECTION	0%	2.0h	2.0h	0.0h	2026-Oct-15 20:00	2026-Oct-15 22:00	0900-IF0003	C275877		
A3860	12M GENERAL INSTRUMENTATION ELECTRICAL INSPECTION	0%	1.0h	1.0h	0.0h	2026-Oct-15 22:00	2026-Oct-15 23:00	0900-EE90061	C275881		
A3870	Change out bolth Latch Position sensor	100%	4.0h	0.0h	0.0h	2026-Oct-08 21:00 A	2026-Oct-09 01:00 A			R10508019	
A3880	Investigate Intermitent failure communication with POD1	75%	24.0h	6.0h	-78.0h	2026-Oct-11 23:00 A	2026-Oct-16 05:00			R10509298	
A3890	Investigate the packer Isolation valves working reverse	100%	12.0h	0.0h	0.0h	2026-Oct-08 01:00 A	2026-Oct-08 13:00 A			R10509299	
A3900	Change Flow Line Position Indicator	100%	2.0h	0.0h	0.0h	2026-Oct-08 13:00 A	2026-Oct-08 15:00 A			R10508020	

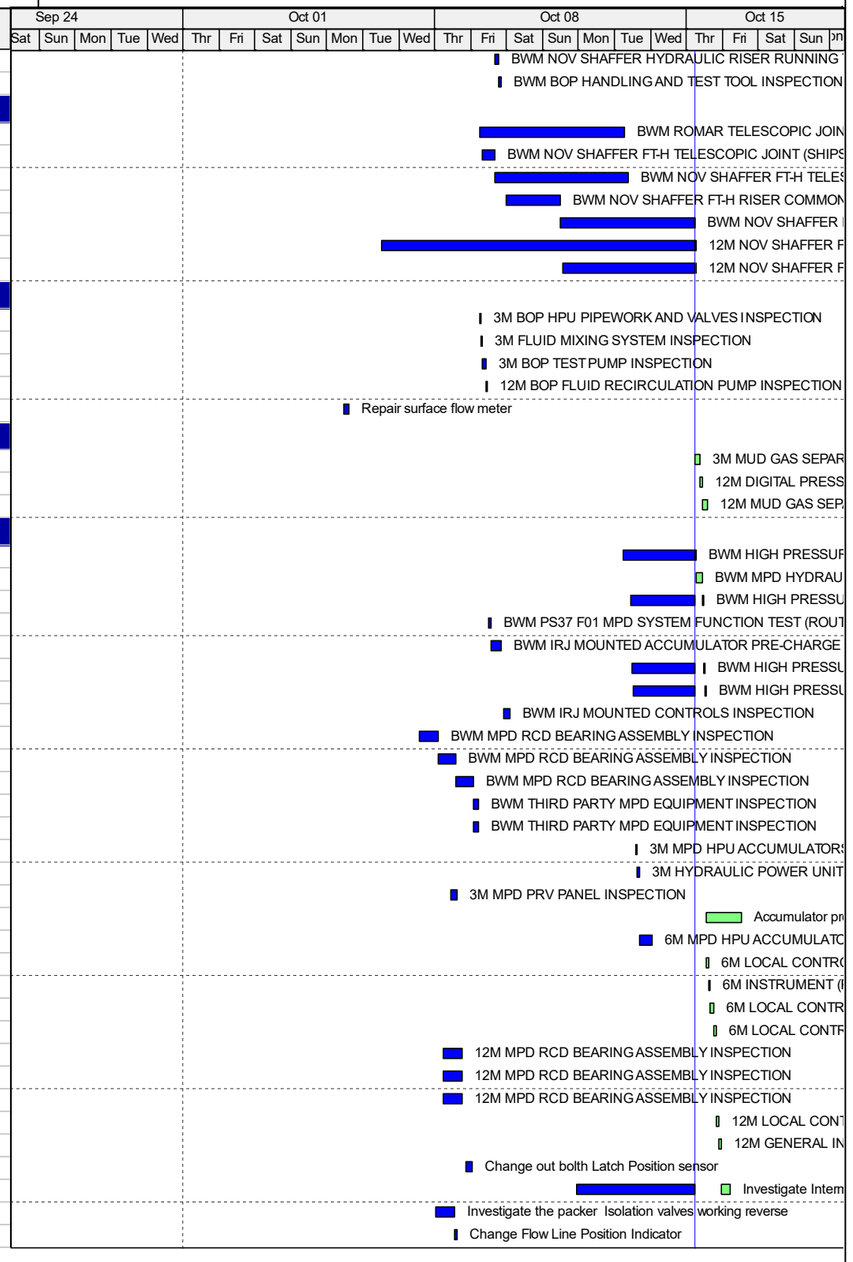

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
	Full Schedule For Review		
