


SACRED to Production — programme chart

Dashboards, scanner, notification loops, Ask SACRED AI, database, training and handover · September 2026 to February 2027 · issued 1 October 2026 by Dan Plant (draft 4: the transfer moves to the week of 19 October; the database is built on Fabric by Dan and needs no IT resource; ISIT to name the production home, the sacred server is the sandbox)

Critical path in red: the scanner leaves Dan's PC for the sacred server in the **week of 19 October 2026** (Houston)
Every bar to the right of it moves day for day with it
Open: sdr1azneuiis01d is the sandbox. ISIT to name the production home and the cutover
Database: built by Dan on Fabric, no IT resource required

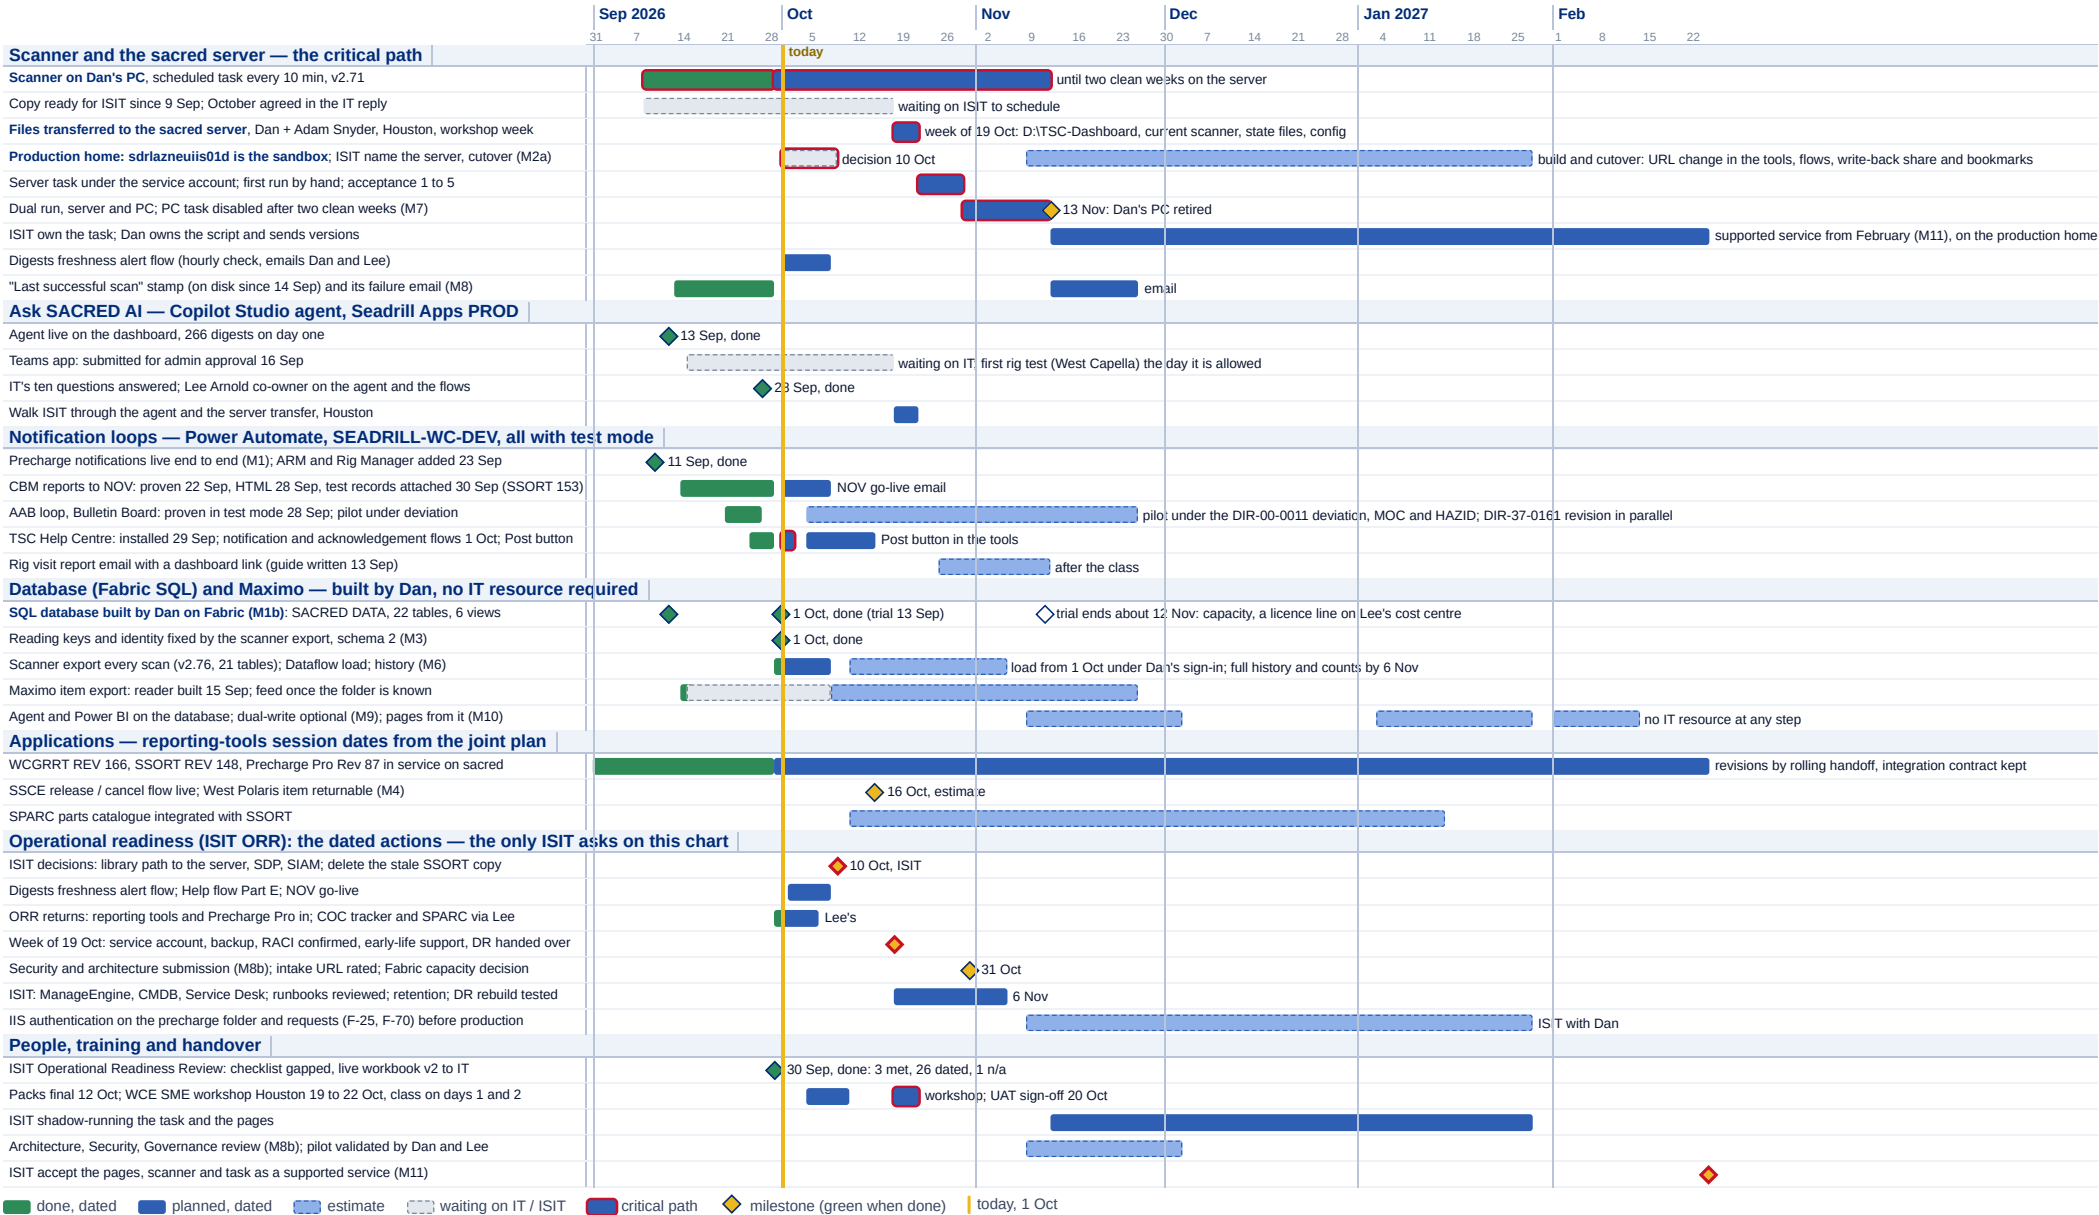

Sources: DASHBOARD - PRODUCTION - TIMELINE - REPLY .md (joint plan with the reporting-tools session, 11 to 14 Sep), IT - REPLY - COPILOT - AGENT - QUESTIONS .md (28 Sep), SCANNER - SERVER - MIGRATION - IT - HANDOFF .md, WEEK - PLAN - 2026 - 09 - 14 .md, DATABASE - BUILD - PLAN .md (1 Oct). Dates marked estimate are not commitments. Page 2 lists the milestones and what changed since the 11 September chart.

Milestones and what changed since the 11 September chart

Milestones

#	Milestone	Date	Gate
M1	Precharge notifications live end to end	11 Sep 2026, done	—
M1a	Ask SACRED AI live: Copilot Studio agent on the scanner's report digests, button on the dashboard	13 Sep 2026, done	Teams publishing: waiting on IT
M1b	SQL database created on Fabric by Dan, no IT resource: trial database 13 Sep; SACRED DATA built 1 Oct, 22 tables and 6 views from the scanner's own export	13 Sep, 1 Oct, done	60-day trial: capacity on Lee's cost centre by mid-November (a licence line, not a resource)
M1c	SPARC handoff received; Maximo answered (daily 06:00 export already exists)	14 Sep 2026, done	landing folder, Manpreet
M1d	CBM to OEM flow proven; AAB loop proven end to end in test mode; TSC Help Centre installed	22 to 29 Sep 2026, done	—
M1e	IT's ten questions answered; Lee Arnold co-owner on the agent and the flows	28 Sep 2026, done	—
M2	Files transferred to the sacred server (D:\TSC-Dashboard), Dan with Adam Snyder in Houston, during the WCE SME workshop week	week of 19 Oct 2026	service account ready
M2a	Production home named by ISIT. The sacred server is the sandbox; after the transfer everything still runs on it. ISIT to say whether it becomes production or a production server is built, and plan the cutover (server name in the tools, flows, write-back share, bookmarks). Build and cutover Nov to Jan, estimate. Not in the ORR.	decision 10 Oct 2026	ISIT Infrastructure
M3	Reading-key and identity conventions fixed: the scanner's normalised export (schema 2) is the contract, file, matchKey and the rig identity as the keys	1 Oct 2026, done	—
M4	SSCE release / cancel flow live; West Polaris item returnable	16 Oct 2026, estimate	reporting-tools session
M5	Server task running every ten minutes under the service account, acceptance checklist 1 to 5 passed; dual run with Dan's PC begins	30 Oct 2026	M2
M6	Scanner normalised export live on every scan (v2.76, 21 tables, 17,751 rows on 1 Oct); Dataflow Gen2 loads it into SACRED DATA hourly under Dan's sign-in; proof is the counts against the manifest	1 Oct, done; load 9 Oct	Dan, no IT
M7	Dan's PC task disabled after two clean weeks; ISIT own the server task	13 Nov 2026	M5
M8	"Last successful scan" failure email in place (the stamp has been on disk since 14 Sep); Digests freshness alert flow in place from early October	27 Nov 2026	—
M8a	Notification flows re-pointed to the IT-provided service identity	when IT provide it	ISIT
M8b	Pilot validated by Dan and Lee; submitted for Architecture, Security and Governance review	Nov 2026, estimate	M5, M8a
M9	Ask SACRED AI and Power BI reading the database; scanner dual-write (optional, once an app registration exists). No IT resource: the database is already provisioned.	Jan 2027, estimate	app registration only if dual-write is wanted
M10	Parity proven: the same pages fed from the database, files as fallback	mid-Feb 2027	M6 + two-week window; an authenticated path to decide, not a provisioning ask
M11	ISIT accept the pages, scanner and task as a supported service, on the production home	Feb 2027	M2a, M7, M8, M10

What changed since the 11 September chart

- **The server transfer has a week and a person: the week of 19 October, Dan with Adam Snyder in Houston.** On the 11 September chart it was "copied, ISIT have not started". The copy is refreshed on the day, so the server gets the current scanner (v2.71 today), the state files and the config.
- **Ask SACRED AI is live** (13 Sep) in Seadrill Apps PROD with web search and general knowledge off. Only the Teams app approval is outstanding, submitted 16 Sep. First rig test (West Capella) the day it is allowed.
- **The database is built, by Dan, with no IT resource.** SACRED DATA is a Fabric SQL database in Dan's workspace (created 1 Oct; 22 tables, 6 views, one needs_attention definition). The scanner writes a normalised export on every run (schema 2: reports, rig checks, CBM, AAB, precharge requests and issued sheets, Help Centre records, SSCE requests, 21 tables) and a Dataflow Gen2 loads it under Dan's own sign-in. Nothing to provision, no secret, nothing installed. The January row is no longer an IT ask: the only cost item is Fabric capacity on Lee's cost centre when the trial ends about 12 November, and an app registration later if the scanner is to write directly.
- **Three more notification loops exist:** CBM reports to NOV (proven 22 Sep, HTML attachment 28 Sep, go-live email to NOV in October), the AAB loop on the Seadrill Bulletin Board (proven end to end in test mode 28 Sep; pilot under a documented deviation with the MOC and HAZID while DIR-37-0161 is revised), and the TSC Help Centre (installed 29 Sep, flow 30 Sep). All share one pattern: post, scanner, page, notification with a dashboard link, receipt.
- **Test mode** is built into every notification flow: while on, only the office list is mailed and the subject says so. No rig or NOV address receives a test.
- **Monitoring:** the scanner writes its last-successful-scan stamp on every complete run (since 14 Sep). The hourly Digests freshness alert promised to IT is built in early October, before the move, and keeps watching after it.
- **Training:** the two-day class in Houston, 19 and 20 October, the same week as the transfer: reporting tools on the Monday; dashboards, precharge process, AAB and Help Centre on the Tuesday. Packs final by 12 October.
- **Scanner today:** v2.71, no modules, nothing installed, reads three SharePoint libraries through OneDrive sync, does a full parse only when something changed (about a second otherwise). The service account needs read on the three report libraries, write on Digests and on the two IIS folders. No secrets, nothing to rotate.
- **Removed from the chart:** the hosted application (Dan, 11 Sep). The programme ends with ISIT accepting the pages, scanner and task as a supported service.
- **Draft 4, 1 October:** the transfer moves from Sunday 18 October to the week of 19 October (the workshop week, Dan in Houston); M5, M7 and M8 move a week with it. New critical item M2a: the sacred server is the sandbox, so even after the transfer nothing runs on a production server until ISIT name one and plan the cutover; it is not in the ORR and is now on the Open actions sheet (v2).
- **Draft 3, 1 October:** the database rows are redrawn. M1b, M3 and the export half of M6 are done; M9 is no longer "first IT resource". The ISIT asks on this chart are now only the service account, the Teams approval, the 10 October decisions and the ORR configuration work.
- **Draft 2, 1 October:** ISIT's Operational Readiness Review was gapped on 30 September (3 of 30 met, 26 dated with owners, 1 not applicable); its dated actions are a new section on page 1, with the ISIT decisions due 10 October, the handover list for the week of 19 October, the security submission by 31 October and the ManageEngine, CMDB and Service Desk configuration by 6 November. SSORT 153 is live and the test records reach NOV (Part D3 proven 30 Sep). The class sits inside Lee Arnold's WCE SME workshop, 19 to 22 October.

Open, waiting on others

- Teams app approval for Ask SACRED AI (IT, submitted 16 Sep).
- Service account for the server task and the notification flows (ISIT, needed by the week of 19 Oct).
- **The production home** (ISIT Infrastructure, decision 10 Oct): the sacred server is the sandbox; is it to become production, or is a production server built, and when is the cutover?
- Where Manpreet's daily 06:00 Maximo export lands (Manpreet, via Dan).
- Fabric capacity on Lee's cost centre by about 12 November (a licence line; no IT engineering resource).
