


SACRED to Production — programme chart

Dashboards, scanner, notification loops, Ask SACRED AI, database, training and handover · September 2026 to February 2027 · issued 30 September 2026 by Dan Plant

Critical path in red: the scanner leaves Dan's PC for the sacred server on **18 October 2026**
Every bar to the right of it moves day for day with it

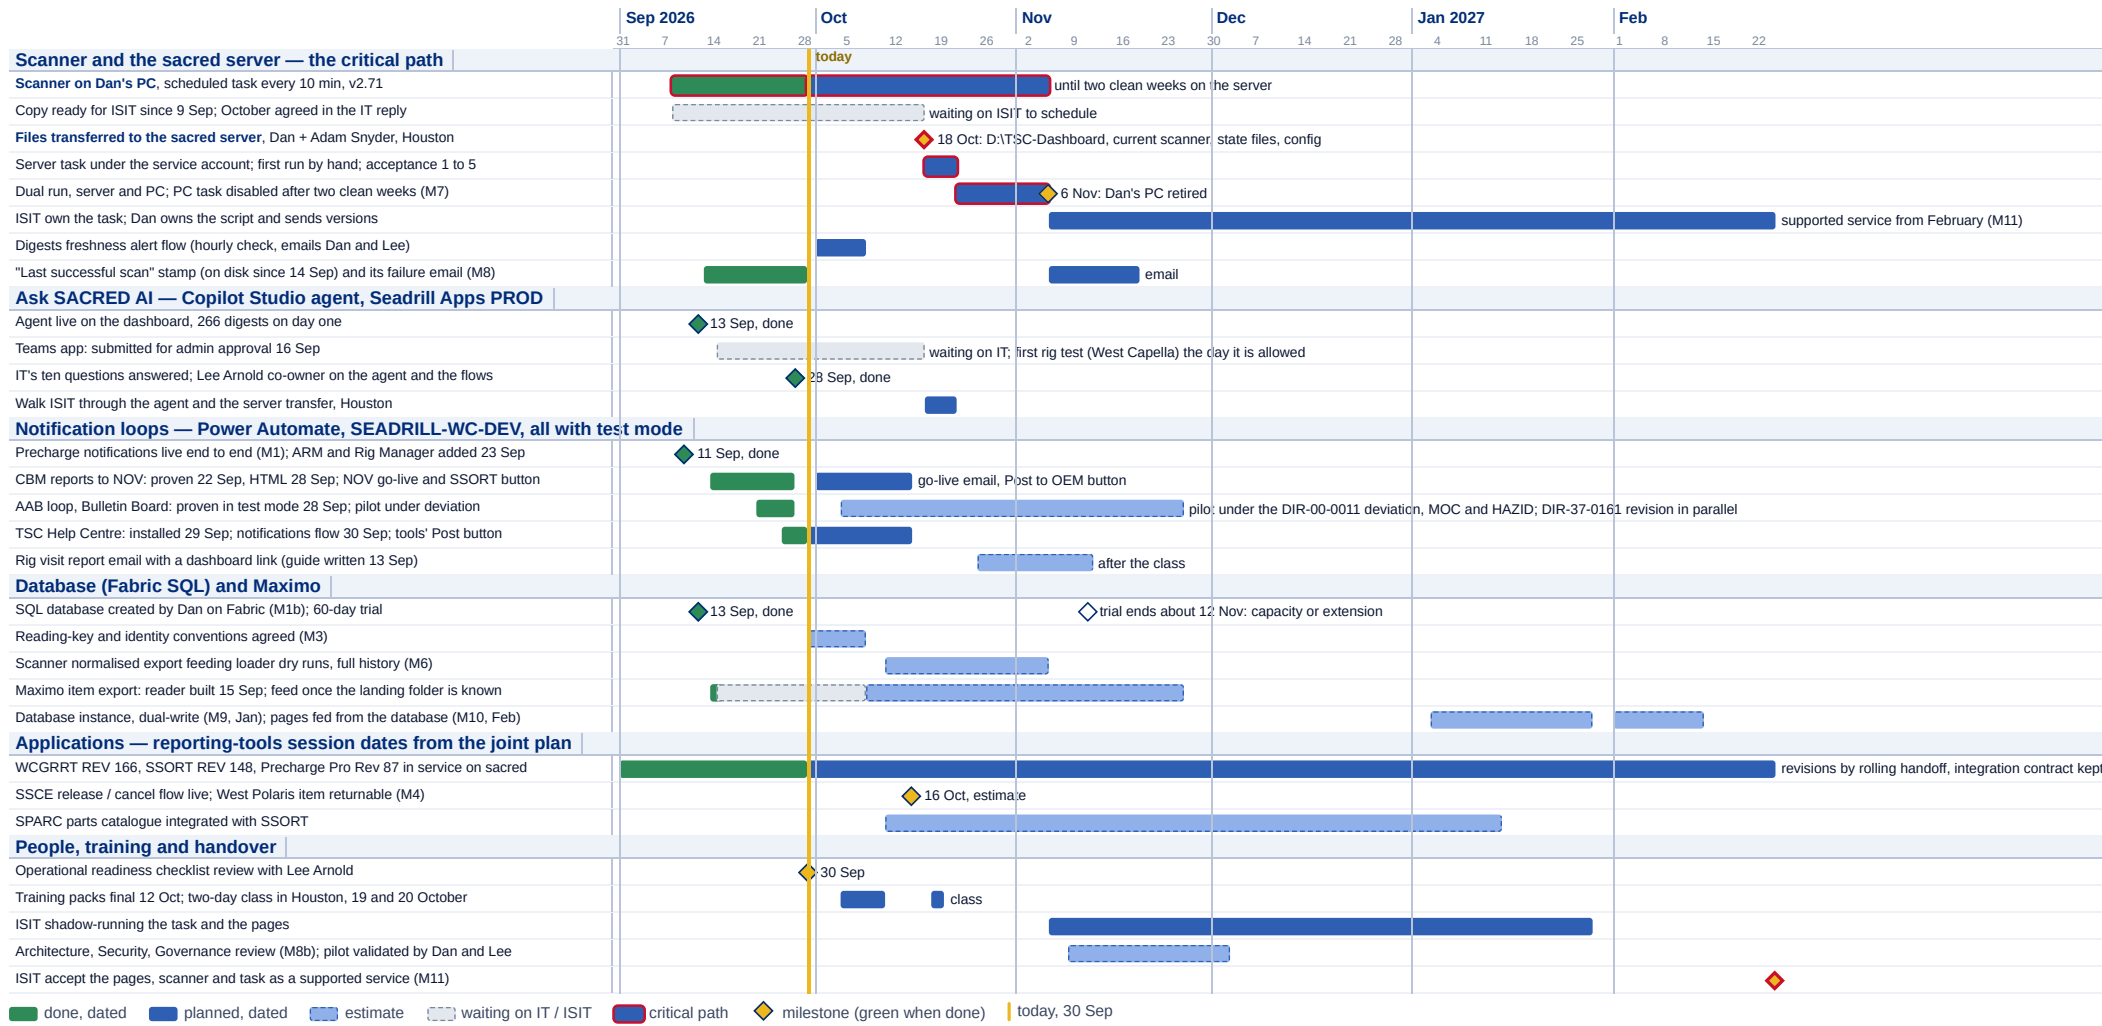

Sources: DASHBOARD-PRODUCTION-TIMELINE-REPLY.md (joint plan with the reporting-tools session, 11 to 14 Sep), IT-REPLY-COPILOT-AGENT-QUESTIONS.md (28 Sep), SCANNER-SERVER-MIGRATION-IT-HANDOFF.md, WEEK-PLAN-2026-09-14.md. Dates marked estimate are not commitments. Page 2 lists the milestones and what changed since the 11 September chart.

Milestones and what changed since the 11 September chart

Milestones

#	Milestone	Date	Gate
M1	Precharge notifications live end to end	11 Sep 2026, done	—
M1a	Ask SACRED AI live: Copilot Studio agent on the scanner's report digests, button on the dashboard	13 Sep 2026, done	Teams publishing: waiting on IT
M1b	SQL database created on Fabric by Dan, no IT resource	13 Sep 2026, done	60-day trial: capacity or extension by mid-November
M1c	SPARC handoff received; Maximo answered (daily 06:00 export already exists)	14 Sep 2026, done	landing folder, Manpreet
M1d	CBM to OEM flow proven; AAB loop proven end to end in test mode; TSC Help Centre installed	22 to 29 Sep 2026, done	—
M1e	IT's ten questions answered; Lee Arnold co-owner on the agent and the flows	28 Sep 2026, done	—
M2	Files transferred to the sacred server (D : \TSC - Dashboard), Dan with Adam Snyder in Houston	18 Oct 2026	service account ready
M3	Reading-key and identity conventions agreed between loader and scanner	9 Oct 2026, estimate	reporting-tools session
M4	SSCE release / cancel flow live; West Polaris item returnable	16 Oct 2026, estimate	reporting-tools session
M5	Server task running every ten minutes under the service account, acceptance checklist 1 to 5 passed; dual run with Dan's PC begins	23 Oct 2026	M2
M6	Scanner normalised export feeding loader dry runs over the full history	6 Nov 2026, estimate	M3
M7	Dan's PC task disabled after two clean weeks; ISIT own the server task	6 Nov 2026	M5
M8	"Last successful scan" failure email in place (the stamp has been on disk since 14 Sep); Digests freshness alert flow in place from early October	20 Nov 2026	—
M8a	Notification flows re-pointed to the IT-provided service identity	when IT provide it	ISIT
M8b	Pilot validated by Dan and Lee; submitted for Architecture, Security and Governance review	Nov 2026, estimate	M5, M8a
M9	Database instance; scanner dual-write on	Jan 2027	first IT resource
M10	Parity proven: the same pages fed from the database, files as fallback	mid-Feb 2027	M9 + two-week window
M11	ISIT accept the pages, scanner and task as a supported service	Feb 2027	M7, M8, M10

Dates marked estimate are not commitments and move with the critical path. Questions: Dan Plant, Technical Superintendent, Well Control Engineering.

What changed since the 11 September chart

- **The server transfer has a date and a person: 18 October, Dan with Adam Snyder in Houston.** On the 11 September chart it was "copied, ISIT have not started". The copy is refreshed on the day, so the server gets the current scanner (v2.71 today), the state files and the config.
- **Ask SACRED AI is live** (13 Sep) in Seadrill Apps PROD with web search and general knowledge off. Only the Teams app approval is outstanding, submitted 16 Sep. First rig test (West Capella) the day it is allowed.
- **The database started in September, not January.** Fabric SQL exists in Dan's workspace on a 60-day trial. The January IT ask is a paid capacity, not an Azure instance. The scanner side (reading keys, normalised export) runs October to November.
- **Three more notification loops exist:** CBM reports to NOV (proven 22 Sep, HTML attachment 28 Sep, go-live email to NOV in October), the AAB loop on the Seadrill Bulletin Board (proven end to end in test mode 28 Sep; pilot under a documented deviation with the MOC and HAZID while DIR-37-0161 is revised), and the TSC Help Centre (installed 29 Sep, flow 30 Sep). All share one pattern: post, scanner, page, notification with a dashboard link, receipt.
- **Test mode** is built into every notification flow: while on, only the office list is mailed and the subject says so. No rig or NOV address receives a test.
- **Monitoring:** the scanner writes its last-successful-scan stamp on every complete run (since 14 Sep). The hourly Digests freshness alert promised to IT is built in early October, before the move, and keeps watching after it.
- **Training:** the two-day class in Houston, 19 and 20 October, the two days after the transfer: reporting tools on the Monday; dashboards, precharge process, AAB and Help Centre on the Tuesday. Packs final by 12 October.
- **Scanner today:** v2.71, no modules, nothing installed, reads three SharePoint libraries through OneDrive sync, does a full parse only when something changed (about a second otherwise). The service account needs read on the three report libraries, write on Digests and on the two IIS folders. No secrets, nothing to rotate.
- **Removed from the chart:** the hosted application (Dan, 11 Sep). The programme ends with ISIT accepting the pages, scanner and task as a supported service.

Open, waiting on others

- Teams app approval for Ask SACRED AI (IT, submitted 16 Sep).
- Service account for the server task and the notification flows (ISIT, needed by 18 Oct).
- Where Manpreet's daily 06:00 Maximo export lands (Manpreet, via Dan).
- Fabric capacity or trial extension by mid-November (IT).
